




FORM 1A

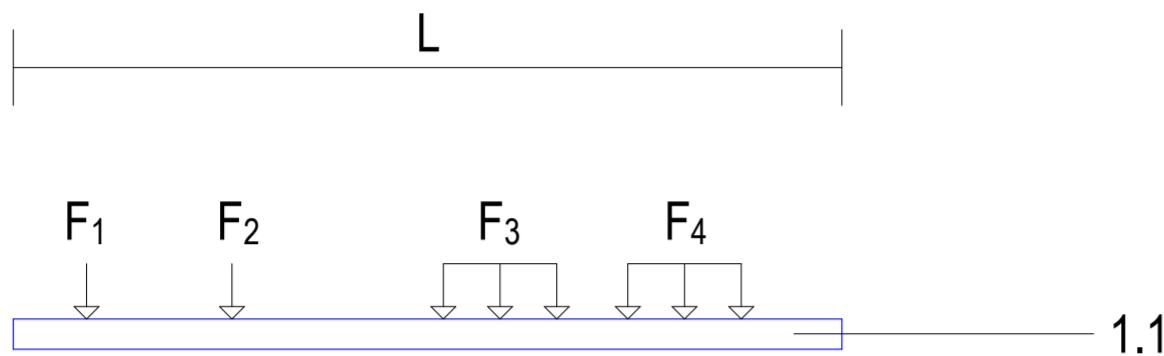

1.1

DATA INPUT FORM

DATA INPUT - SIZING				DATA INPUT - LOADS					
Item	Un	Value	Validated	Item	Un	Value	Max Span (m)	Value (kN)	Validated
L	mm	2650		F1	kN/m	2.2000	3.6	7.9200	
				F2	kN/m	2.2000	3.6	7.9200	
				F4	kN/m	1.0297	1.2	1.23564	
				F3	kN/m	1.0297	1.2	1.23564	

Horizontal Profiles	Type:	Rod	Pressix CC 41	siFramo 80/30	siFramo 80	siFramo 100
	L _{max} (mm)	Cut Length (mm)	Max. Loads (kN)			
1500	1487		1.17	7.55	13.33	40.29
2000	1983		0.66	4.25	7.50	22.66
2650	2650		0.37	2.42	4.27	12.91
3000	2977		0.29	1.89	3.33	10.07
Profile ID	Formula	Profile Selection				
1.1	F ₁ +F ₂ +F ₃ +F ₄					
Horizontal Loads Calculation Method			Vertical Loads Calculation Method			
Point Load	Example:	Load Distribution Assumption	Example:	Notes:	1. Initial Assumptions:	2. For this case:
	For a horizontal beam with a Length of 1000mm, the Maximum Loads supported for the different configuration of Loads are the following:					
Distributed Load	- Single Point Load - 12.06 kN - Distributed Load - 24.13 kN/m - 2 Point Load - 18.10 kN - 3 Point Load - 18.09 kN					
2 Point Loads	Based on these values, for the purpose of this Catalogue, we will consider that the Load will always be a Point Load in the center of the beam, which is the worst case scenario.					
3 Point Loads						
	F ₂ [kN] as a permanent load over L					

NOTE:

FORM2A Production:

Defines primary and secondary support component sizes, types and part numbers.

Scope Exclusion:

Frame interface with the building structure is not included in this document.

For comprehensive guidelines and additional information, contact the project management team.

OVERVIEW

MC Prefab is a collaborative joint venture between CTS, MECWIDE, and BIMMS. The primary objective of this partnership is to streamline the production of Mechanical, Electrical, and Plumbing (MEP) support structures.

To achieve standardization and optimization in support production, installation, and to minimize material waste, a comprehensive catalog of solutions has been developed. This catalog defines all support solutions along with their respective variables.

Process Stages:

The overall process of MEP support structure production and installation is divided into three distinct stages:

1-Preparation

2-Production

3-Installation

Each stage requires specific documentation, outlined as follows:

Form1A: Base Specification for Support Solution Definition

Form2A: Fabrication Drawing


Form3A: Installation Drawing

These documents ensure the standardization and efficiency of the entire process, from initial preparation through to final installation.

For any further details or clarifications, please refer to the MC Prefab documentation guidelines or contact the project management team.

Naming Convention

DC.FWA.COR.1.1-1A



P02	03/12/2024	Issued For Information	GJ	JT
P01	08/11/2024	Issued For Information	GJ	JT
Rev.	Date	Description	Sign.	Veri.

JOINT VENTURE:

MC Prefab
Nordics

DESIGN & BUILD PARTNERS:

CTS Nordics

BIMMS
integrated engineering

MECWIDE
ENGINEERING CHALLENGES

DRAWING NAME:	DC.FWA.COR.4.1-1A		
DRAWING STATUS:	Issued For Information		
DATE CREATED:	08/11/2024	LAST REV. DATE:	03/12/2024
SIGNED:	GJ	CONTROL:	JT
DRAWING NUMBER:	FIN3005-BMS-XX-XX-DR-J-14111	FORMAT:	P02
Order Amount	65	REVISION:	A2
